Project: G18001-1
Layout: Mjoskabel Daily Work without BL

Customer: Eidsiva Nett AS
Confidential - ABB Employes Only

Data Date: 2018-05-30
Print Date: 2018-05-30

Activity ID	Unique ID MP	INT/EXT	Activity Name	% Complete	Orig Dur	Start	Finish
G18001-1 Mjöskabeln (COPY - relations removed) - Current					10344	2018-03-20	2019-05-25
G18001-1.1 Milestones					10344	2018-03-20	2019-05-25
G18001-1.1.2 Contractual Milestones					10344	2018-03-20	2019-05-25
G18001-1.1.2.4 Early Works Agreement					408	2018-03-20	2018-04-06
175019_2220		EXT	Supplier Selection	0%	0	2018-03-20*	
175019_1100		EXT	Early Works Agreement	0%	0	2018-04-04*	
175019_2240		EXT	Client to approve cable design	0%	0	2018-04-04	
175019_2250		EXT	NKT to start placement of purchasing orders for cable materials Measure	0%	0	2018-04-06	
175019_2260		EXT	NKT to start production preparation Measure	0%	0	2018-04-04	
G18001-1.1.2.1 General					5184	2018-04-18	2018-11-20
175019_2230		EXT	G1 - Contract Signing	0%	0	2018-04-27	
175019_1310		EXT	G2 - Project Management Documents	0%	0		2018-05-19
175019_1410		EXT	G3 - Master Document Register issued to Company for review	0%	0		2018-04-18
175019_1470		EXT	G4 - Detailed route engineering complete and accepted by Company	0%	0		2018-08-01*
175019_1520		EXT	G5 - Cable system engineering complete and accepted by Company	0%	0		2018-05-01
175019_1610		EXT	G7 - Site Acceptance Test completed	0%	0		2018-11-20
175019_2280		EXT	OHL Start de-energization	0%	0	2018-09-14	
175019_2290		EXT	OHL End de-energization	0%	0		2018-11-19
G18001-1.1.2.2 Work Package A					7104	2018-04-10	2019-01-31
175019_1200		EXT	WPA1 - Placement of purchasing order copper	0%	0	2018-04-10	
175019_1020		EXT	WPA2 - Start manufacturing of cables	0%	0	2018-05-07	
175019_1320		EXT	WPA3 - FAT Cables	0%	0		2018-09-02
175019_1480		EXT	WPA5 - Cables & accessories delivered to Oslo	0%	0		2018-10-05
175019_1190		EXT	WPA7 - Mounting of cable end terminations and fitting in stands on site(s) completed	0%	0		2018-11-14
175019_2090		EXT	WPA8 - As-built documentation	0%	0		2019-01-31*
G18001-1.1.2.3 Work Package B					6792	2018-08-15	2019-05-25
175019_1650		EXT	WPB1 - Installation engineering complete and submitted to Company	0%	0		2018-08-15
175019_1560		EXT	WPB2 - Construction of new landfall at Jessnes completed	0%	0		2018-09-28
175019_1740		EXT	WPB3 - Construction of new landfall at Snekkersveen completed	0%	0		2018-10-05
175019_1750		EXT	WPB4 - Construction of new landfall at Engelandsodden completed	0%	0		2018-08-31
175019_1760		EXT	WPB5 - Construction of new landfall at Tangnesodden completed	0%	0		2018-09-14
175019_1770		EXT	WPB6 - Mobilisation of installation spread completed at Mjösa	0%	0		2018-10-06
175019_1780		EXT	WPB7 - Partial Recovery of Jessnes-Snekkersveen	0%	0		2018-10-05
175019_1790		EXT	WPB8 - Partial Recovery of Bråstad-Heggenhaugen link completed	0%	0		2019-05-25
175019_1800		EXT	WPB9 - Installation of Jessnes-Snekkersveen link completed	0%	0		2018-10-25
175019_1810		EXT	WPB10 - Installation of Engelandsodden - Tangnesodden link completed	0%	0		2018-10-20
175019_1580		EXT	WPB11 -As-built documentation	0%	0		2019-01-31
G18001-1.1.3 Payment Milestones					9840	2018-04-10	2019-05-25
G18001-1.1.3.1 General					0	2018-11-20	2018-11-20
175019_2000		EXT	G7 - Site Acceptance Test completed	0%	0		2018-11-20
G18001-1.1.3.2 Work Package A					7104	2018-04-10	2019-01-31
175019_2010		EXT	WPA1 - Placement of purchasing order copper	0%	0	2018-04-10	

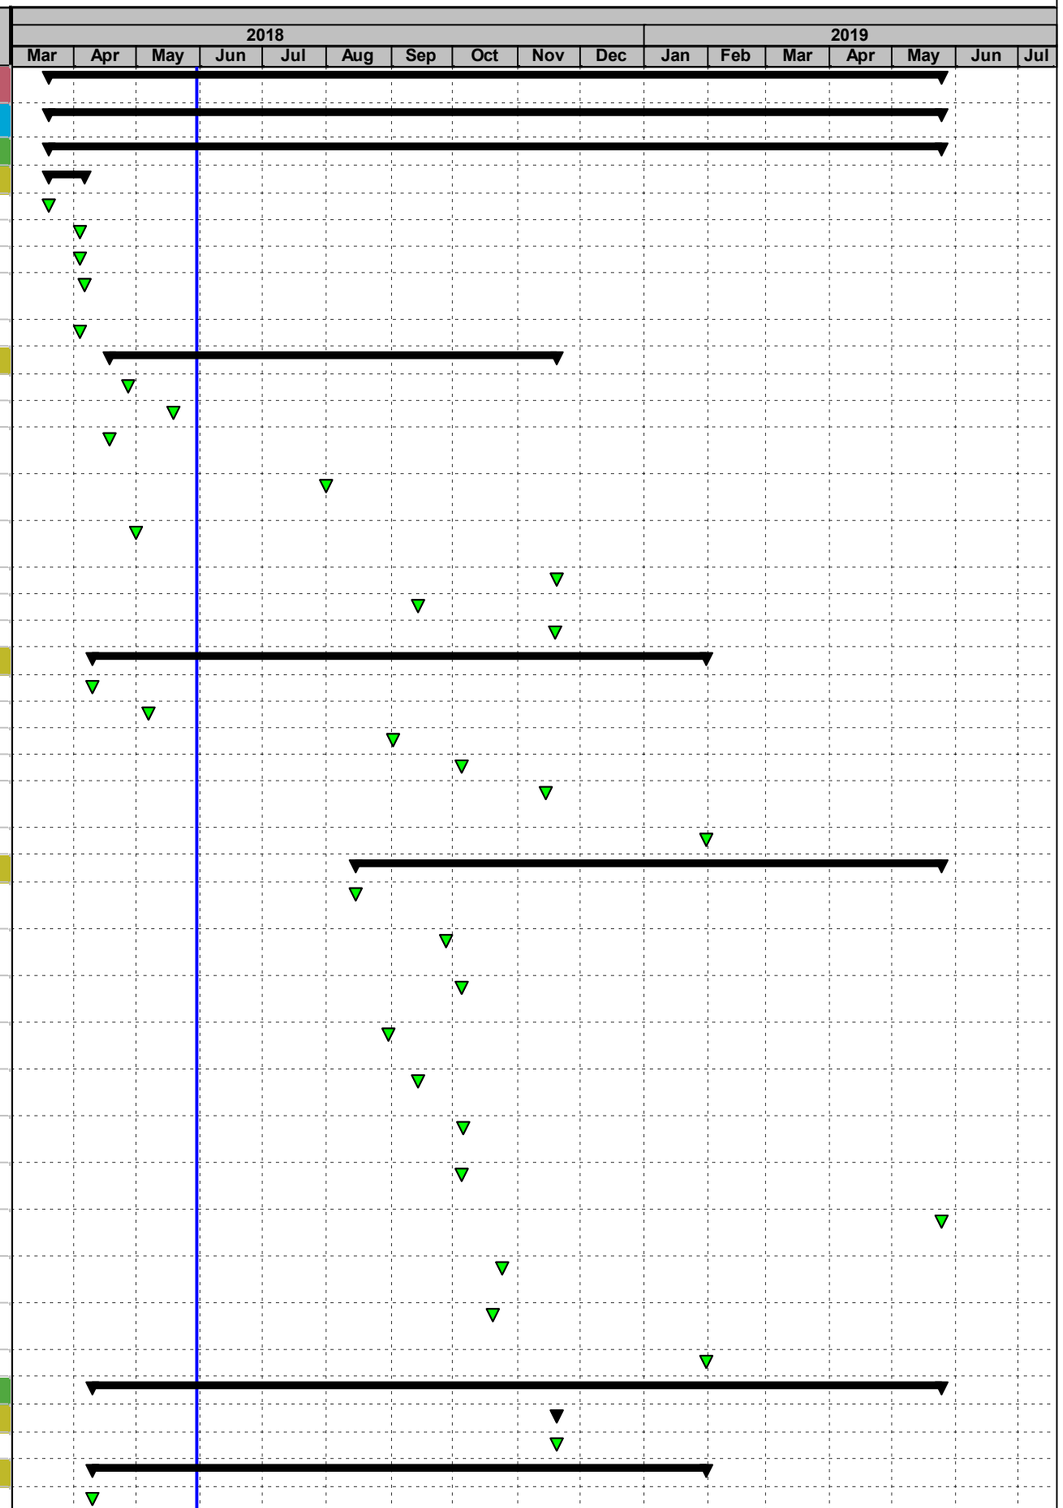

Remaining Level of Effort | WBS sum rem | WBS Sum ac | Actual Level of Effort | R...

Date	Revision	Checked	Approved

Project: G18001-1
Layout: Mjoskabel Daily Work without BL

Customer: Eidsiva Nett AS
Confidential - ABB Employes Only

Data Date: 2018-05-30
Print Date: 2018-05-30

Activity ID	Unique ID MP	INT/EXT	Activity Name	% Complete	Orig Dur	Start	Finish
175019_2020		EXT	WPA2 - Start manufacturing of cables	0%	0	2018-05-07	
175019_2030		EXT	WPA3 - FAT Cables	0%	0		2018-09-02
175019_2040		EXT	WPA5 - Cables & accessories delivered to Oslo	0%	0		2018-10-05
175019_1590		EXT	WPA8 - As-built documentation	0%	0		2019-01-31
175019_2300		EXT	WPA9 - Extrusion Completed	0%	0		2018-05-25
G18001-1.1.3.3 Work Package B					6792	2018-08-15	2019-05-25
175019_2060		EXT	WPB1 - Installation engineering complete and submitted to Company	0%	0		2018-08-15
175019_2070		EXT	WPB3 - Construction of new landfall at Snekkersveen completed	0%	0		2018-10-05
175019_2080		EXT	WPB5 - Construction of new landfall at Tangnesodden completed	0%	0		2018-09-14
175019_2050		EXT	WPB11 -As-built documentation	0%	0		2019-01-31
175019_2310		EXT	WPB12 - Finalization of removal of old oil cables Gjövik	0%	0		2019-05-25
G18001-1.1.5 Penalty Milestones					792	2018-09-02	2018-10-05
G18001-1.1.5.1 Work Package A					792	2018-09-02	2018-10-05
175019_1700		EXT	WPA3 - FAT Cables	0%	0		2018-09-02
175019_1720		EXT	WPA5 - Cables & accessories delivered to Oslo	0%	0		2018-10-05
G18001-1.1.6 Milestones for Calling off Options					2304	2018-04-27	2018-08-01
G18001-1.1.6.2 Work Package B					2304	2018-04-27	2018-08-01
175019_2320		EXT	Option 1 - Crossing option/7C	0%	0		2018-06-01*
175019_2330		EXT	Option 2 - Pre-lay survey	0%	0		2018-04-27*
175019_2350		EXT	Option 3 - Post-lay survey	0%	0		2018-08-01*
175019_2340		EXT	Option 4 - UXO survey	0%	0		2018-04-27*
175019_2360		EXT	Option 5 - Extra distance (spacers) crossing with Telenor cable	0%	0		2018-06-01*
G18001-1.4 Engineering and Documentation					3192	2018-04-04	2018-08-15
G18001-1.4.4 Documentation					360	2018-05-04	2018-05-19
G18001-1.4.4.1 Project Management					360	2018-05-04	2018-05-19
175019_1010		EXT	Contract schedule baseline, first draft	0%	0	2018-05-04	
175019_1180		EXT	Progress monitoring system	0%	0	2018-05-19	
175019_1290		EXT	Cost control procedure	0%	0	2018-05-04	
G18001-1.4.4.3 QHSE					0	2018-05-04	2018-05-04
175019_1000		EXT	Quality plan	0%	0	2018-05-04	
175019_1170		EXT	HSE programme	0%	0	2018-05-04	
175019_1300		EXT	Quality surveillance plan	0%	0	2018-05-04	
G18001-1.4.2 Engineering					3192	2018-04-04	2018-08-15
G18001-1.4.2.11 Cable & Accessories Engineering					768	2018-04-04	2018-05-06
G18001-1.4.2.11.20 Cable & Accessories Design					768	2018-04-04	2018-05-06
175019_1090		EXT	Detailed Engineering	0%	648	2018-04-04	2018-05-01
175019_1250		EXT	Technical Preparation Cable & Accessories	0%	648	2018-04-04	2018-05-01
175019_1360		EXT	ERP Preparation Cable & Accessories	0%	120	2018-05-01	2018-05-06
G18001-1.4.2.7 Installation					3192	2018-04-04	2018-08-15
175019_1930		EXT	Engineering and planning phase	0%	3192	2018-04-04	2018-08-15
G18001-1.3 Procurement					2400	2018-04-06	2018-07-15
G18001-1.3.2 Production Material					2400	2018-04-06	2018-07-15
175019_1080		EXT	Leadtime production material	0%	672	2018-04-06	2018-05-04
175019_1350		EXT	Leadtime accessories	0%	1680	2018-05-06	2018-07-15
G18001-1.6 Manufacturing					3336	2018-05-07	2018-09-23
G18001-1.6.13 Manufacturing					3336	2018-05-07	2018-09-23
G18001-1.6.13.20 Manufacturing					3336	2018-05-07	2018-09-23
175019_1380		EXT	Manufacturing Offshore Cable	0%	3336	2018-05-07	2018-09-23

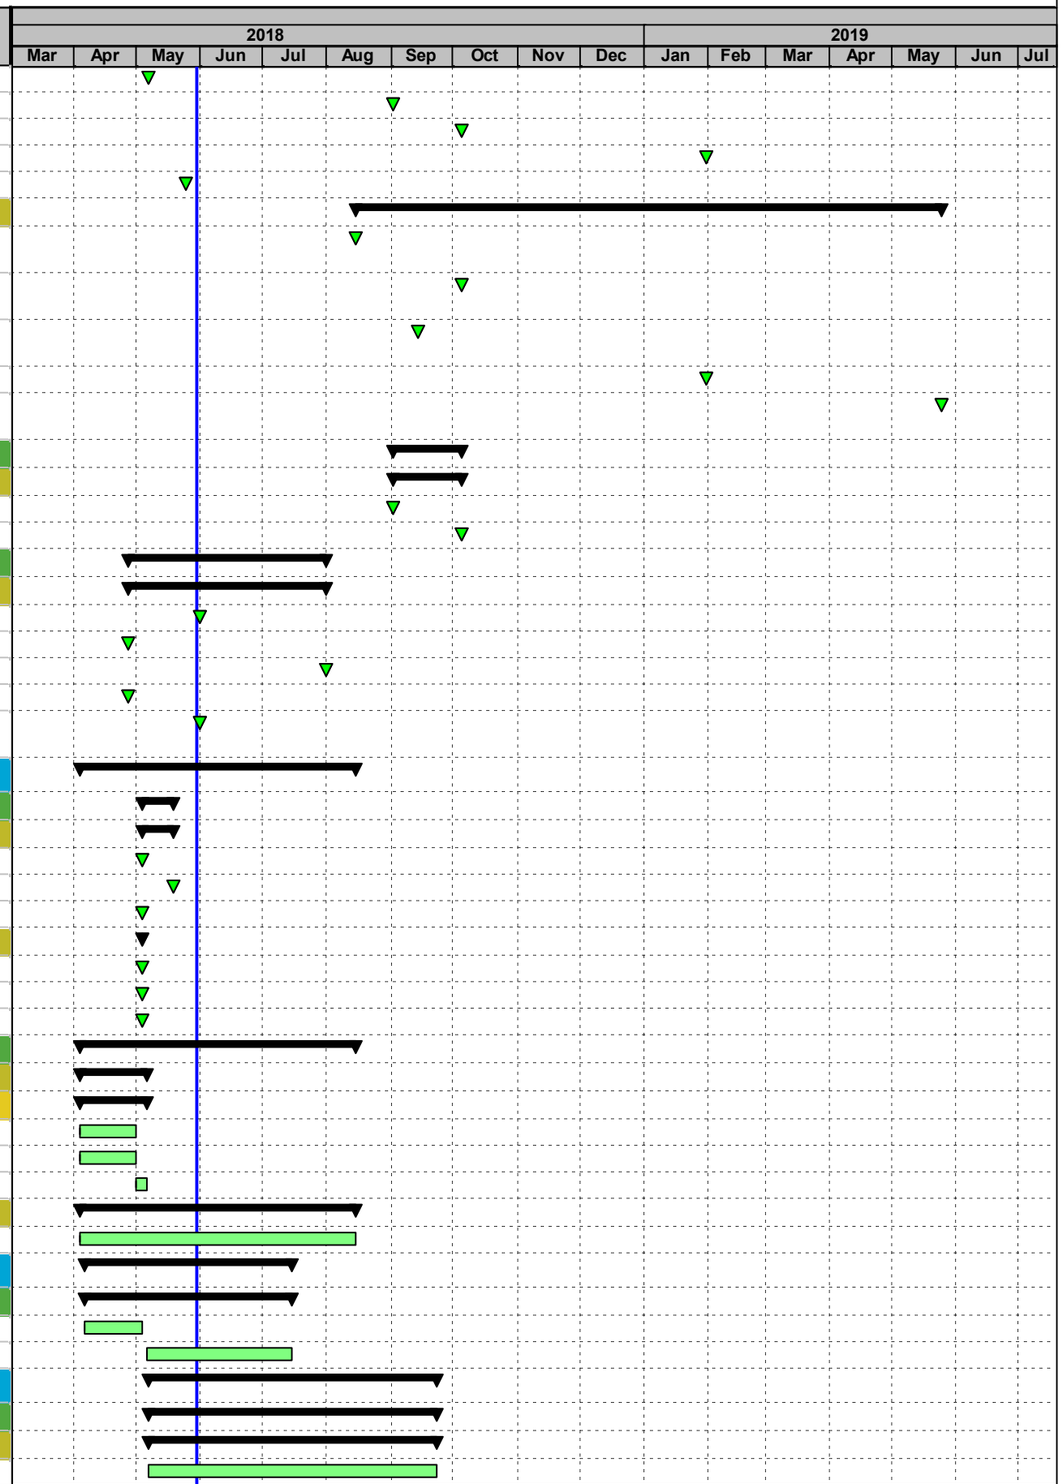

Remaining Level of Effort | WBS sum rem | WBS Sum ac | Actual Level of Effort | R...

Date	Revision	Checked	Approved

Project: G18001-1
Layout: Mjoskabel Daily Work without BL

Customer: Eidsiva Nett AS
Confidential - ABB Employes Only

Data Date: 2018-05-30
Print Date: 2018-05-30

Activity ID	Unique ID MP	INT/EXT	Activity Name	% Complete	Orig Dur	Start	Finish
G18001-1.7 Store and Deliver					144	2018-09-30	2018-10-06
G18001-1.7.3 Load out					48	2018-09-30	2018-10-02
175019_1130		EXT	Cable load out in Karlskrona	0%	48	2018-09-30	2018-10-02
G18001-1.7.4 Transportation					96	2018-10-02	2018-10-06
175019_2120		EXT	Cable transportation to "Drammen" (Oslo due to weight and bridges)	0%	72	2018-10-02	2018-10-05
175019_2270		EXT	Cable transportation to Site at Mjosa, every 2nd night, starting with 2 drums on site at:	0%	24	2018-10-05	2018-10-06
G18001-1.9 Installation					8520	2018-06-04	2019-05-25
G18001-1.9.13 Mjöskabel Installation 2018					4056	2018-06-04	2018-11-20
G18001-1.9.13.4 Installation (including testing)					4056	2018-06-04	2018-11-20
G18001-1.9.13.4.1 Survey Pre-lay and or UXO (Option)					240	2018-06-04	2018-06-14
175019_1940		EXT	Mobilisation of vessel	0%	24	2018-06-04*	2018-06-05
175019_3080		EXT	Survey	0%	192	2018-06-05*	2018-06-13
175019_3090		EXT	Demobilisation	0%	24	2018-06-13*	2018-06-14
G18001-1.9.13.4.2 Enabling works Gjöviksfjord (new cables)					720	2018-08-15	2018-09-14
175019_3100		EXT	Mobilisation of Excavators & equipment (Gensets, Welfare containers) at Gjövik	0%	72	2018-08-15*	2018-08-18
175019_3110		EXT	Preparation of accesses for road at Engelandsodden side	0%	72	2018-08-18*	2018-08-21
175019_3120		EXT	Excavation of Pipes for 7 cables up to Vault location 75m long foreseen	0%	168	2018-08-21*	2018-08-28
175019_3130		EXT	Preparation of landfall 10x8x1m for vault	0%	72	2018-08-28*	2018-08-31
175019_3140		EXT	Move to Tangnesodden side	0%	24	2018-08-31*	2018-09-01
175019_3150		EXT	Preparation of accesses for road at Tangnesodden	0%	72	2018-09-01*	2018-09-04
175019_3160		EXT	Excavation of Pipes for 7 cables up to Vault location 75m long foreseen	0%	168	2018-09-04*	2018-09-11
175019_1950		EXT	Preparation of landfall 10x8x1m for vault location+Move to Jessnes	0%	72	2018-09-11*	2018-09-14
G18001-1.9.13.4.3 Enabling works Furnesfjord (old oil cables)					168	2018-09-14	2018-09-21
175019_3180		EXT	Excavation/removal of Culverts for 6 cables up to Termination locations 50m long foreseen at Jessnes	0%	72	2018-09-14*	2018-09-17
175019_3170		EXT	Move to Nes side	0%	24	2018-09-17*	2018-09-18
175019_1960		EXT	Excavation/removal of Culverts for 6 cables up to Termination locations 50m long foreseen at Nes	0%	72	2018-09-18*	2018-09-21
G18001-1.9.13.4.4 Oilfilled cables work					336	2018-09-21	2018-10-05
175019_3240		EXT	Deconnection and suction of oil for 6 cables at Furnesfjord	0%	192	2018-09-21*	2018-09-29
175019_3210		EXT	Mobilisation of Decommissioning cut & seal vessel	0%	192	2018-09-21*	2018-09-29
175019_3200		EXT	Retrieval & cutting at-20m of 6 oilcables at Jessnes side	0%	48	2018-09-29*	2018-10-01
175019_3190		EXT	Moving to port & unloading retrieved cables	0%	12	2018-10-01*	2018-10-01
175019_3220		EXT	Retrieval & cutting at -20m of 6 oilcables at Nes side	0%	48	2018-10-01*	2018-10-03
175019_3230		EXT	Moving to port & unloading retrieved cables	0%	12	2018-10-03*	2018-10-04
175019_1980		EXT	Demobilisation of Decommissioning cut & seal equipment	0%	24	2018-10-04*	2018-10-05
G18001-1.9.13.4.5 Enabling works Furnesfjord (new cables)					336	2018-09-21	2018-10-05
175019_3250		EXT	Preparation of accesses (road + Terminations) at Jessnes	0%	24	2018-09-21*	2018-09-22
175019_3260		EXT	Excavation of Culverts for 7 cables up to Termination locations 50m long foreseen	0%	72	2018-09-22*	2018-09-25

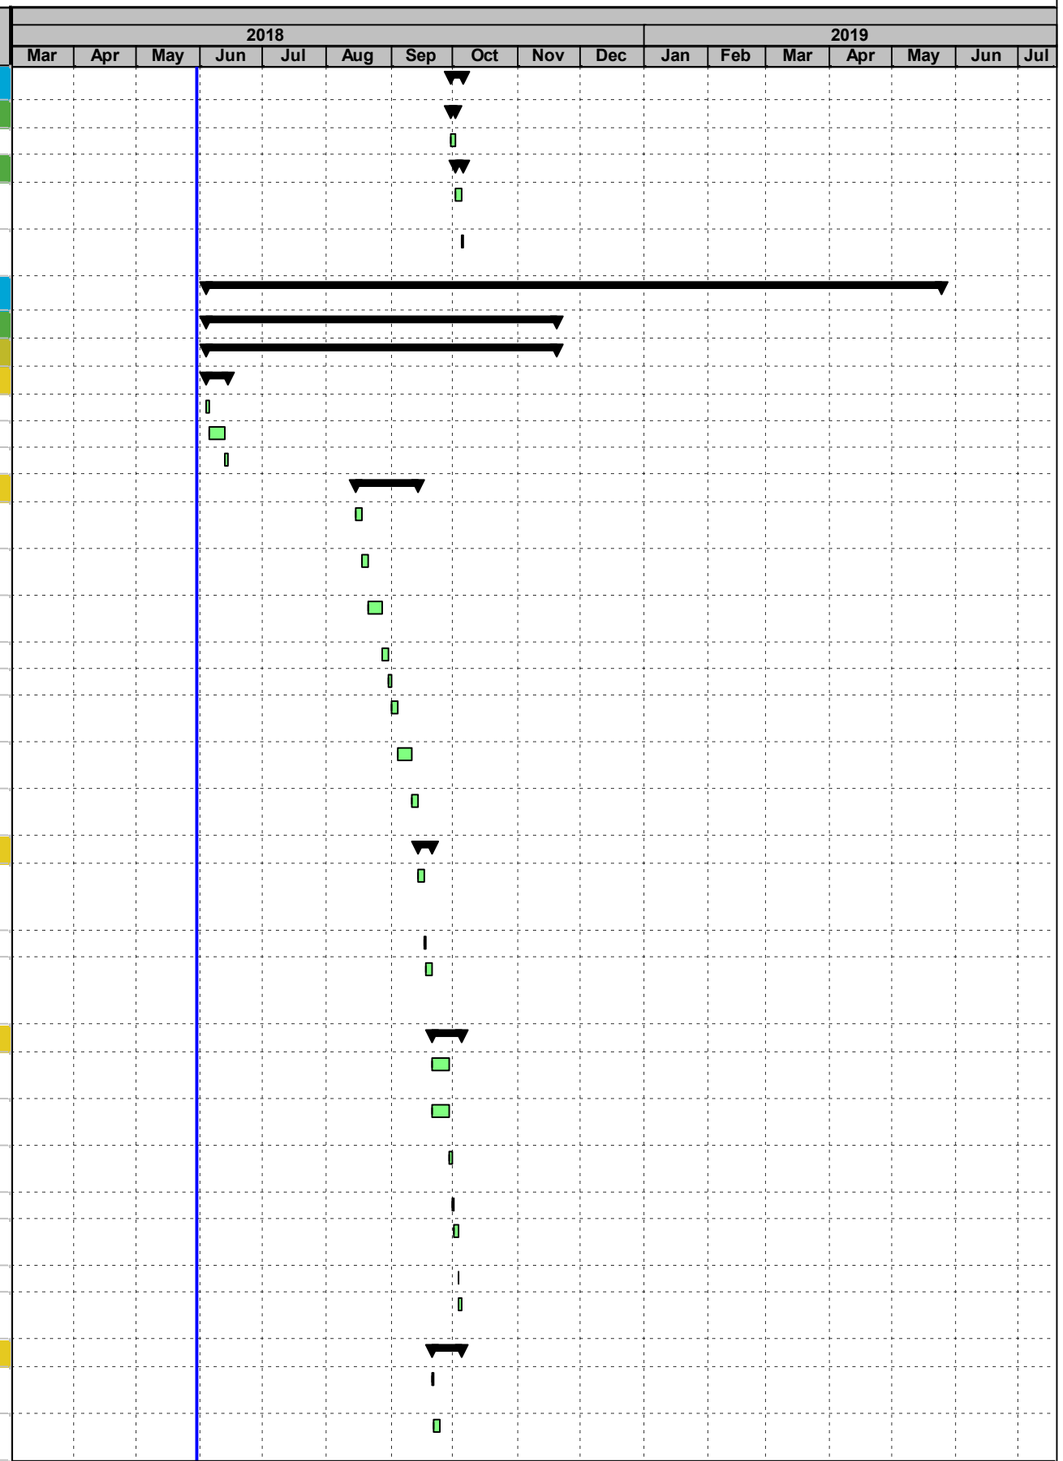

Remaining Level of Effort | WBS sum rem | WBS Sum ac | Actual Level of Effort | R...

Date	Revision	Checked	Approved

Project: G18001-1
Layout: Mjoskabel Daily Work without BL

Customer: Eidsiva Nett AS
Confidential - ABB Employes Only

Data Date: 2018-05-30
Print Date: 2018-05-30

Activity ID	Unique ID MP	INT/EXT	Activity Name	% Complete	Orig Dur	Start	Finish
175019_3270		EXT	Preparation of Termination foundations(7)+including mounting of columns + Hangoffs	0%	72	2018-09-25*	2018-09-28
175019_3280		EXT	Move to Nes side	0%	0	2018-09-28*	
175019_3290		EXT	Preparation of accesses (road + Terminations) at Nes	0%	24	2018-09-28*	2018-09-29
175019_3300		EXT	Excavation of Culverts for 7 cables up to Termination locations 50m long foreseen	0%	72	2018-09-29*	2018-10-02
175019_1990		EXT	Preparation of Termination foundations(7)+including mounting of columns + Hangoffs	0%	72	2018-10-02*	2018-10-05
G18001-1.9.13.4.6			**Cable Laying of HVAC Cables 2x7 cables 2500/2400m**		1080	2018-09-26	2018-11-10
175019_2200		EXT	Mobilisation of cable laying equipment incl. DollyBase building at CLV barge	0%	240	2018-09-26*	2018-10-06
175019_1070		EXT	1st Loading of Cable drum, Beach Pull In at GJöviksfjord	0%	12	2018-10-06	2018-10-06
175019_2400		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-06	2018-10-07
175019_2470		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-07	2018-10-08
175019_2410		EXT	2nd Loading of Cable drum, Beach Pull In	0%	12	2018-10-08	2018-10-08
175019_2420		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-08	2018-10-09
175019_2480		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-09	2018-10-10
175019_2430		EXT	3rd Loading of Cable drum, Beach Pull In	0%	12	2018-10-10	2018-10-10
175019_2440		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-10	2018-10-11
175019_2490		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-11	2018-10-12
175019_2450		EXT	4th Loading of Cable drum, Beach Pull In	0%	12	2018-10-12	2018-10-12
175019_2460		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-12	2018-10-13
175019_2500		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-13	2018-10-14
175019_2510		EXT	5th Loading of Cable drum, Beach Pull In	0%	12	2018-10-14	2018-10-14
175019_2520		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-14	2018-10-15
175019_2530		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-15	2018-10-16
175019_2540		EXT	6th Loading of Cable drum, Beach Pull In	0%	12	2018-10-16	2018-10-16
175019_2550		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-16	2018-10-17
175019_2560		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-17	2018-10-18
175019_2570		EXT	7thLoading of Cable drum, Beach Pull In	0%	12	2018-10-18	2018-10-18
175019_2580		EXT	Cable Laying incl mounting of CPS at 250m/h	0%	24	2018-10-18	2018-10-19
175019_2590		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-19	2018-10-20
175019_2130		EXT	Move to Furnesfjord	0%	12	2018-10-20	2018-10-20
175019_2600		EXT	1st Loading of Cable drum, Beach Pull In	0%	1	2018-10-20	2018-10-20
175019_2610		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-10-20	2018-10-21
175019_2620		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-21	2018-10-22
175019_2630		EXT	2nd Loading of Cable drum, Beach Pull In	0%	12	2018-10-22	2018-10-22
175019_2640		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-10-22	2018-10-23
175019_2650		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-23	2018-10-24
175019_2660		EXT	3rd Loading of Cable drum, Beach Pull In	0%	12	2018-10-24	2018-10-24
175019_2670		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-10-24	2018-10-25
175019_2680		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-25	2018-10-26
175019_2690		EXT	4th Loading of Cable drum, Beach Pull In	0%	11	2018-10-26	2018-10-26
175019_2700		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-10-26	2018-10-27
175019_2710		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-27	2018-10-28
175019_2720		EXT	5th Loading of Cable drum, Beach Pull In	0%	12	2018-10-28	2018-10-28
175019_2730		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-10-28	2018-10-29
175019_2740		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-29	2018-10-30
175019_2750		EXT	6th Loading of Cable drum, Beach Pull In	0%	12	2018-10-30	2018-10-30
175019_2760		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-10-30	2018-10-31
175019_2770		EXT	Beach Pull In, unloading of drum	0%	12	2018-10-31	2018-11-01
175019_2780		EXT	7thLoading of Cable drum, Beach Pull In	0%	12	2018-11-01	2018-11-01

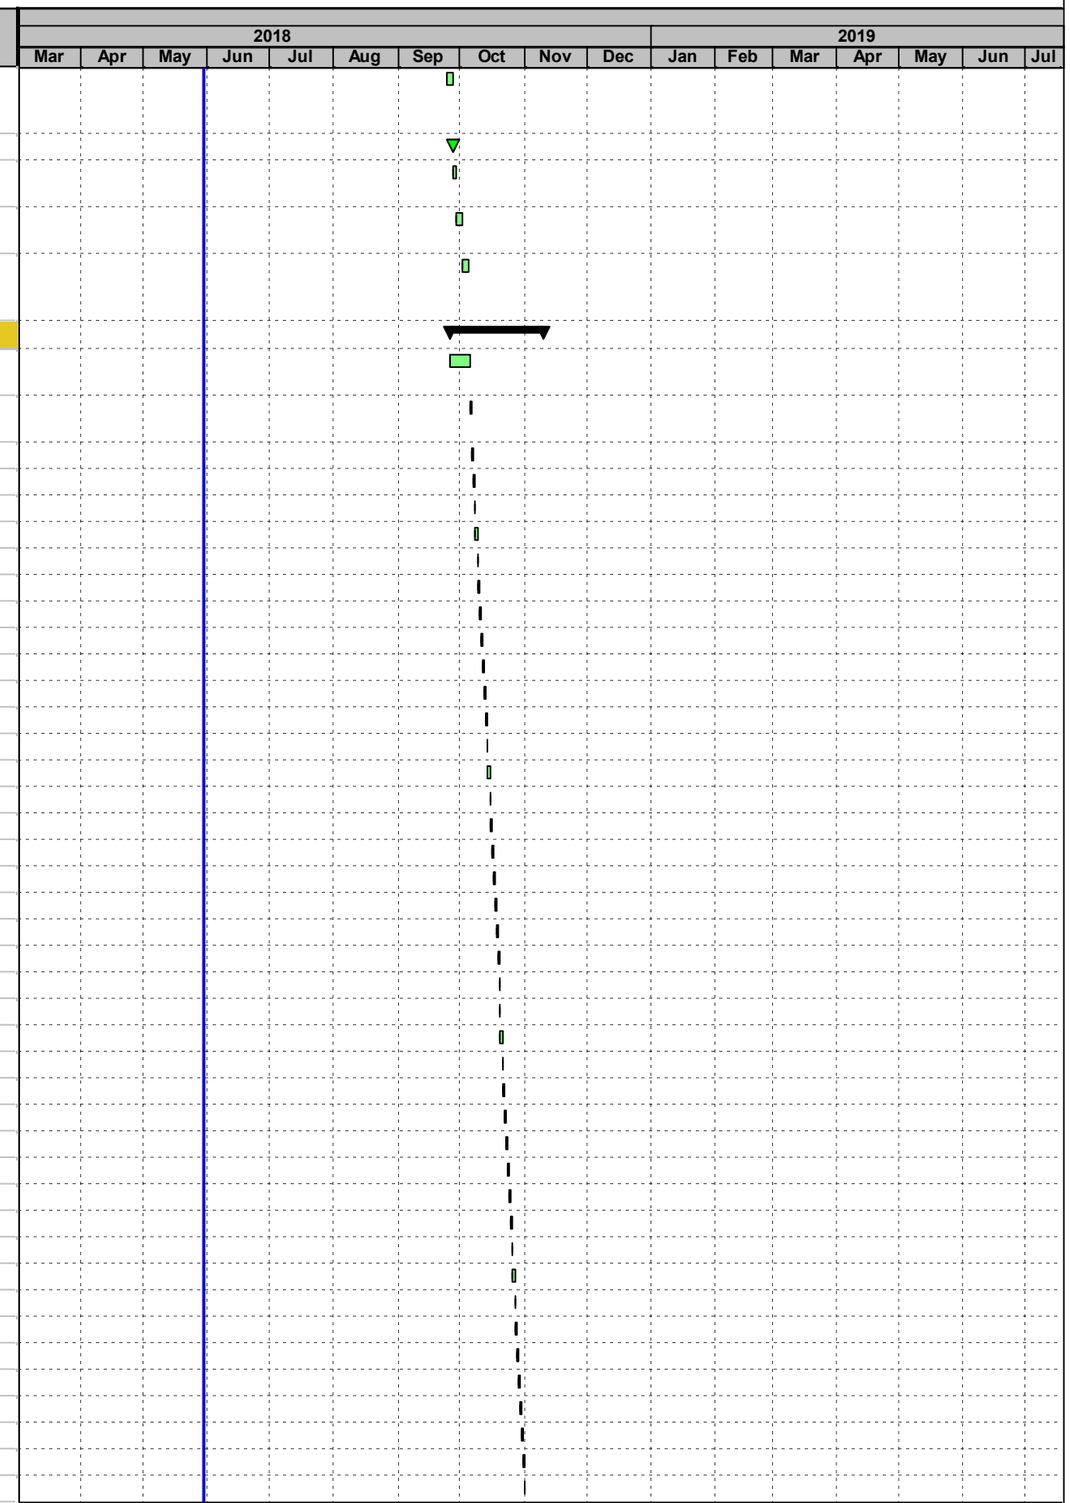

Remaining Level of Effort | WBS sum rem | WBS Sum ac | Actual Level of Effort | R...

Date	Revision	Checked	Approved

Project: G18001-1
Layout: Mjoskabel Daily Work without BL

Customer: Eidsiva Nett AS
Confidential - ABB Employes Only

Data Date: 2018-05-30
Print Date: 2018-05-30

Activity ID	Unique ID MP	INT/EXT	Activity Name	% Complete	Orig Dur	Start	Finish
175019_2790		EXT	Cable Laying incl mountin of CPS at 250m/h	0%	24	2018-11-01	2018-11-02
175019_2800		EXT	Beach Pull In, unloading of drum	0%	12	2018-11-02	2018-11-03
175019_2140		EXT	Demobilisation of laying equipment and dismounting of Laying Barge	0%	168	2018-11-03	2018-11-10
G18001-1.9.13.4.6.1 Post-Lay Survey (Option)					120	2018-11-03	2018-11-08
175019_2370		EXT	Mobilisation of vessel	0%	24	2018-11-03	2018-11-04
175019_2380		EXT	Post-Lay Survey	0%	72	2018-11-04	2018-11-07
175019_2390		EXT	Demobilisation	0%	24	2018-11-07	2018-11-08
G18001-1.9.13.4.9 Cable transportation					144	2018-09-30	2018-10-06
175019_3320		EXT	Cable load out Karlskrona	0%	48	2018-09-30*	2018-10-02
175019_3330		EXT	Cable transportation to "Drammen" (Oslo due to weight and bridges)	0%	72	2018-10-02	2018-10-05
175019_3340		EXT	Cable transportation to Site at Mjosa, every 2nd night, starting with 2 drums on site at:	0%	24	2018-10-05	2018-10-06
G18001-1.9.13.4.7 Jointing and Termination work					816	2018-10-11	2018-11-14
175019_1280		EXT	Mobilise Jointing Equipment/ container at Engelandsodden and Tangnesvika Side (Gjöviksfjord)	0%	24	2018-10-11*	2018-10-12
175019_2810		EXT	Straightening/heating of conductors (7 conductors) (Engelandsodden)	0%	24	2018-10-12	2018-10-13
175019_2820		EXT	Jointingwork (4 cables)	0%	96	2018-10-12	2018-10-16
175019_2830		EXT	Jointingwork (3 cables)	0%	96	2018-10-16	2018-10-20
175019_2840		EXT	Demobilise Jointing Equipment	0%	24	2018-10-20	2018-10-21
175019_2850		EXT	Straightening/heating of conductors (7 conductors) Tangnesvika	0%	24	2018-10-19	2018-10-20
175019_2860		EXT	Jointingwork (4 cables)	0%	96	2018-10-19	2018-10-23
175019_2870		EXT	Jointingwork (3 cables)	0%	96	2018-10-23	2018-10-27
175019_2150		EXT	Demobilise Jointing Equipment & Tents at Gjöviksfjord	0%	24	2018-10-27	2018-10-28
175019_2880		EXT	Build Termination Tents/Prepare Terminations (2 sides)	0%	24	2018-10-26	2018-10-27
175019_2890		EXT	Straightening/heating of conductors (7 conductors) (Jessnes)	0%	24	2018-10-27	2018-10-28
175019_2900		EXT	Termination work (4 cables)	0%	96	2018-10-28	2018-11-01
175019_2910		EXT	Termination work (3 cables)	0%	96	2018-11-01	2018-11-05
175019_2920		EXT	Demobilise Jointing Equipment/move equipment to Nes side+build Jointing tents	0%	48	2018-11-05	2018-11-07
175019_2930		EXT	Straightening/heating of conductors (7 conductors) (Nes)	0%	24	2018-11-04	2018-11-05
175019_2940		EXT	Termination work (4 cables)	0%	72	2018-11-05	2018-11-08
175019_2950		EXT	Termination work (3 cables)	0%	96	2018-11-08	2018-11-12
175019_2170		EXT	Demobilise Termination Equipment	0%	48	2018-11-12	2018-11-14
G18001-1.9.13.4.8 Backfilling and Trenching work & clean up of sites					576	2018-10-26	2018-11-19
175019_2960		EXT	Remaining backfilling & trenching work & clean up of sites at Gjöviksfjord sites	0%	96	2018-10-26*	2018-10-30
175019_2970		EXT	Remaining backfilling & trenching work & clean up of sites at Furnesfjord sites	0%	96	2018-11-11*	2018-11-15
175019_1400		EXT	Demobilisation of excavators and equipment for doing the installation	0%	96	2018-11-15*	2018-11-19
G18001-1.9.13.4.10 SAT test					144	2018-11-14	2018-11-20
175019_3360		EXT	Mobilisation	0%	24	2018-11-14*	2018-11-15
175019_3370		EXT	SAT test	0%	96	2018-11-15	2018-11-19
175019_3350		EXT	Demob	0%	24	2018-11-19	2018-11-20
G18001-1.9.14 Mjöskabel Installation 2019					576	2019-05-01	2019-05-25
G18001-1.9.14.1 Enabling works Gjöviksfjord (Old oilcables)					168	2019-05-01	2019-05-08
175019_1970		EXT	Excavation/removal of Culverts for 6 cables up to Termination locations 50m long foreseen Heggenhaugen	0%	72	2019-05-01*	2019-05-04

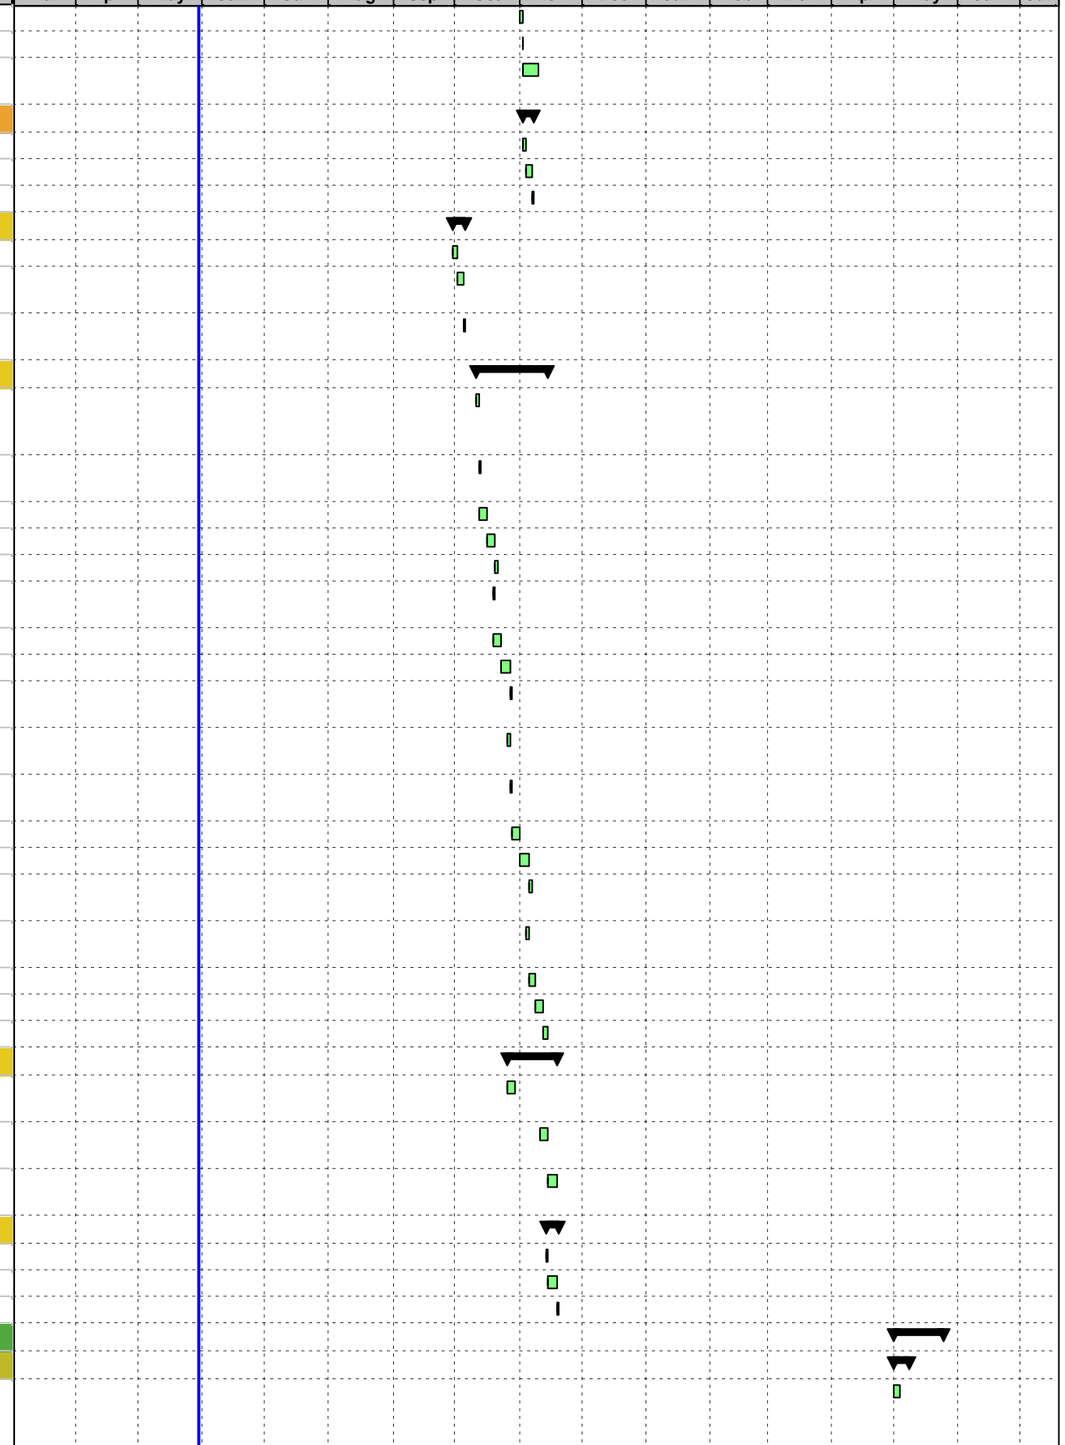

Remaining Level of Effort | WBS sum rem | WBS Sum ac | Actual Level of Effort | R...

Date	Revision	Checked	Approved

Project: G18001-1
Layout: Mjoskabel Daily Work without BL

Customer: Eidsiva Nett AS
Confidential - ABB Employes Only

Data Date: 2018-05-30
Print Date: 2018-05-30

Activity ID	Unique ID MP	INT/EXT	Activity Name	% Complete	Orig Dur	Start	Finish
175019_2980		EXT	Move to Bråvik side	0%	24	2019-05-04	2019-05-05
175019_2990		EXT	Excavation/removal of Culverts for 6 cables up to Termination locations 50m long foreseen Bråvik	0%	72	2019-05-05	2019-05-08
G18001-1.9.14.2 Oilfilled cables work					408	2019-05-08	2019-05-25
175019_3000		EXT	Deconnection and suction of oil for 6 cables at Gjöviksfjord	0%	192	2019-05-08	2019-05-16
175019_3010		EXT	Mobilisation of Decommissioning cut & seal vessel	0%	192	2019-05-08	2019-05-16
175019_3020		EXT	Retrieval & cutting at -20m of 6 oilcables at Heggenhaugen side	0%	48	2019-05-16	2019-05-18
175019_3030		EXT	Moving to port & unloading retrieved cables	0%	12	2019-05-18	2019-05-18
175019_3040		EXT	Retrieval & cutting at -20m of 6 oilcables at Bråvik side	0%	48	2019-05-18	2019-05-20
175019_3050		EXT	Moving to port & unloading retrieved cables	0%	12	2019-05-20	2019-05-21
175019_2210		EXT	Demobilisation of Decommissioning cut & seal equipment	0%	96	2019-05-21	2019-05-25
G18001-1.9.14.3 Clean up of sites					120	2019-05-18	2019-05-23
175019_2180		EXT	Remaining backfilling & trenching work & clean up of sites at Gjöviksfjord sites	0%	120	2019-05-18	2019-05-23
G18001-1.10 Commissioning & Testing					144	2018-11-14	2018-11-20
G18001-1.10.1 Site Acceptance Test					144	2018-11-14	2018-11-20
175019_3060		EXT	Mobilisation	0%	24	2018-11-14	2018-11-15
175019_3070		EXT	SAT test	0%	96	2018-11-15	2018-11-19
175019_1060		EXT	Demob	0%	24	2018-11-19	2018-11-20

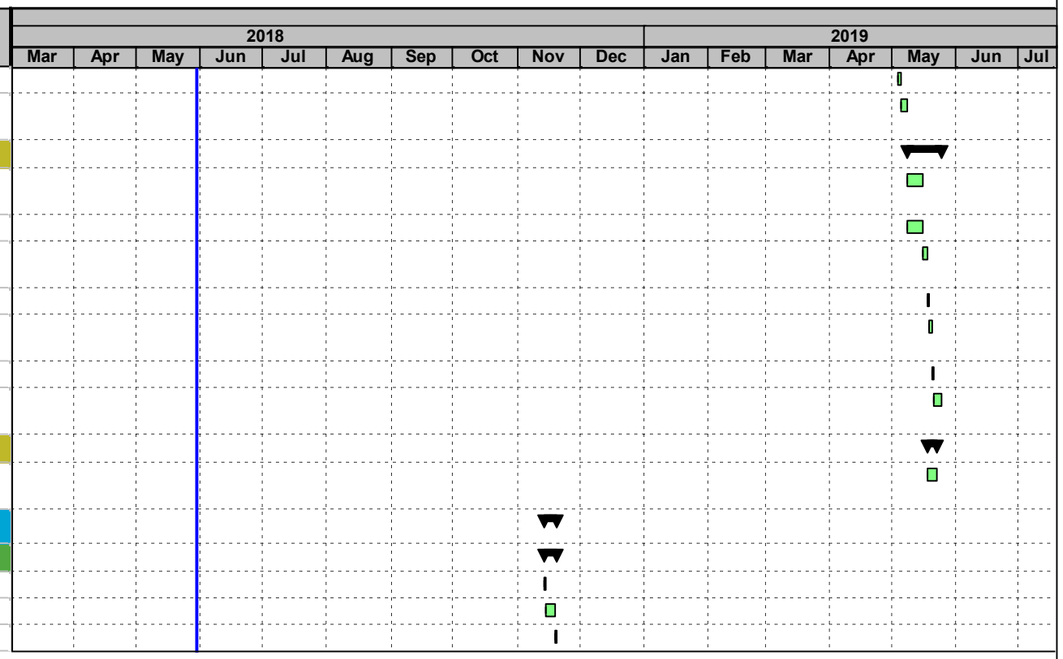

Date	Revision	Checked	Approved
